
American River Common Features Natomas Basin



APRIL 2025

Levee Improvement Project Update

REACH	SCHEDULE
Reach A Gateway Oaks Dr to Farm Rd	 FY25 Construction season to commence on April 15 along Garden HWY starting at Farm Road and extending to City Sump 160. Overhead utility relocations are ongoing, with completion estimated for Winter 2025-2026. Improvements to Pumping Plant 1B Outfall Structure are anticipated to begin in 2025. Visit Reach A website for the latest project news: www.natomaslevees.com
Reach B San Juan Rd to Elverta Rd	 Construction completed in March 2024. I-5 Window - Construction physically complete in November 2023. Pumping Plants: Pumping Plant #3 – Construction completed, and plant is operational. Pumping Plant #5 - Construction anticipated to begin in 2026. Riverside Pumping Plant Replacement ongoing, with discharge pipe relocation projected to begin in 2026. Elkhorn Pumping Plant construction projected to begin in 2027.
Reach C Elverta Rd to Sankey Rd	 Levee construction was completed in 2008/2009 by Sacramento Area Flood Control Agency. Pritchard Lake Pumping Plant construction projected to begin in 2028.
Reach D Sankey Rd to Howsley Rd	 Levee construction was completed in 2008/2009 by Sacramento Area Flood Control Agency. Highway 99 Window – Construction began Summer 2024. Anticipate road closures and traffic impacts beginning early Summer 2025. Pumping Plant #4 – Construction began August 2021; estimated completion by Fall 2025.
Reach E Howsley Rd to Sankey Rd	 Construction activities began June 2023; estimated completion is Fall 2025. Cutoff wall installation completed as of July 19, 2024.
Reach F&G Sankey Rd to Drainage Pumping Station	Levee construction and improvements to the levee slope and Pumping Plant #6 projected to begin in 2028.
Reach H Drainage Pumping Station to Northgate Blvd	Levee construction and improvements to Pumping Stations #8 and #102 began 2018; Patrol Road and Retaining Wall completed in December 2023.
Reach I Northgate Blvd to Gateway Oaks	 Contract 1: Levee construction and improvements to Pump Station #58 completed Fall 2022. Contract 2: Landside levee improvements and installation of maintenance road projected to begin in 2026. Utility Relocations ongoing. Completion expected in 2025.

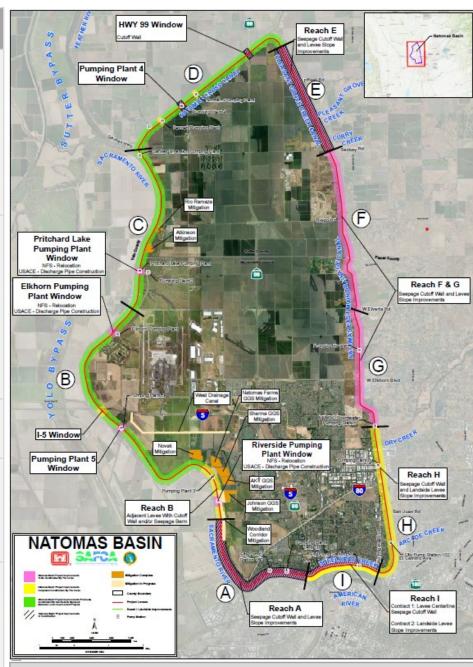

Get the Latest Natomas Updates Here

www.natomaslevees.com







CONTACT INFORMATION

For questions or concerns, please contact USACE Public Affairs 916.557.5100 / spk-pao@usace.army.mil







