



# American River Common Features 2016 Sacramento River Levees Monthly Update

NOVEMBER 2024

## Highlights (last 30 days)

### Sacramento River Erosion (SRE) Contract 2:

All rock placement and in-stream woody material has been completed (see map on the next page).

### Sacramento River Erosion (SRE) Contract 4:

Contract 4 has reached the halfway point in placing soil bioengineering material. The first layer of levee protection is complete, and the second and third layers are now in progress .

**Sacramento River East Levee (SREL):** Contract 4 construction is complete and the contractor is performing minor cleanup work. All public areas have been reopened for public use.

## Looking Ahead (next 30+ days)

### What can I expect?

#### **SRE Sacramento River Erosion Contract 2 Site 1 Option Work:**

Site 1 (The work around Pioneer Bridge) is being moved to a Contract 5 due to real estate acquisition issues and is constructed is planned for Summer of 2025.

**Contract 2:** Will be completing the sump 63 work, placement of soil material and soil-filled quarry stone at site 4 and 5. The construction contractor is aiming to complete work by mid-November, with demobilization beginning in December.

**Contract 4:** Located just downstream of Contract 1, which is just downstream of the Westin Hotel) will be finishing up the placement of rock, topsoil, and coir blocks through mid-November and will start willow pole plantings in late November.

**Revegetation:** Hydroseeding and irrigation on Contract 1 and Contract 2 Season 1 Sites (2, 3 and 6a) has begun and will continue with the planting of native plants, shrubs and trees through November. When planting is complete the site will enter an establishment period of five years, during which the site will be irrigated, maintained, and monitored for performance.

#### **SREL Seepage, Stability, and Overtopping**

USACE is working on completing designs for SREL Contract 5, currently on schedule for construction in 2026.

## Question of the Month

### *With SRE Contracts 2 and 4 construction wrapping up, what's next?*

SRE Contract 2 and 4 erosion work is finishing up and plans are in place to start revegetation for Contract 2 Year 2 and Contract 1 repair area in late spring 2025. Additionally, riparian plantings for Contract 4 will begin at the same time. SRE Site 1 that was previously an option on Contract 2 will become Contract 5 and will begin construction in summer of 2025. In the meantime, to prepare for C5's season you will most likely see tree-trimming in January 2025 and site prep in July 2024. Contract 3 was delayed due to issues with National Environmental Policy Act documentation and is now expected to be constructed in the summer of 2026, spanning two seasons. Tree clearing for Contract 3 is expected to start in November 2025.

### Information Resources:

#### **Project Webpage:**

[www.sacleveeupgrades.com](http://www.sacleveeupgrades.com)



#### **Sacramento District Homepage:**

[www.spk.usace.army.mil](http://www.spk.usace.army.mil)

#### **Contact Information:**

For questions or concerns, please contact our Public Affairs Office at  
916-557-5100

[spk-pao@usace.army.mil](mailto:spk-pao@usace.army.mil)

## Upcoming Milestones

### **Seepage/Stability/ Overtopping**

#### **SREL Contract 4**

Construction  
April 2023 - June 2024

#### **SREL Contract 5**

Construction :  
2026

### **Erosion**

#### **Contract 2**

Construction  
July 2023—November 2024

#### **Contract 3**

Construction Contract Award  
Anticipated January/February  
2026

#### **Contract 4**

Construction  
July 2024 - November 2024


#### **Contract 5**

Construction:  
2025

Additional information can be found on  
our project web page at  
[www.sacleveeupgrades.com](http://www.sacleveeupgrades.com)

\*All Dates Subject to Change

# Erosion Contract 2 Construction Map

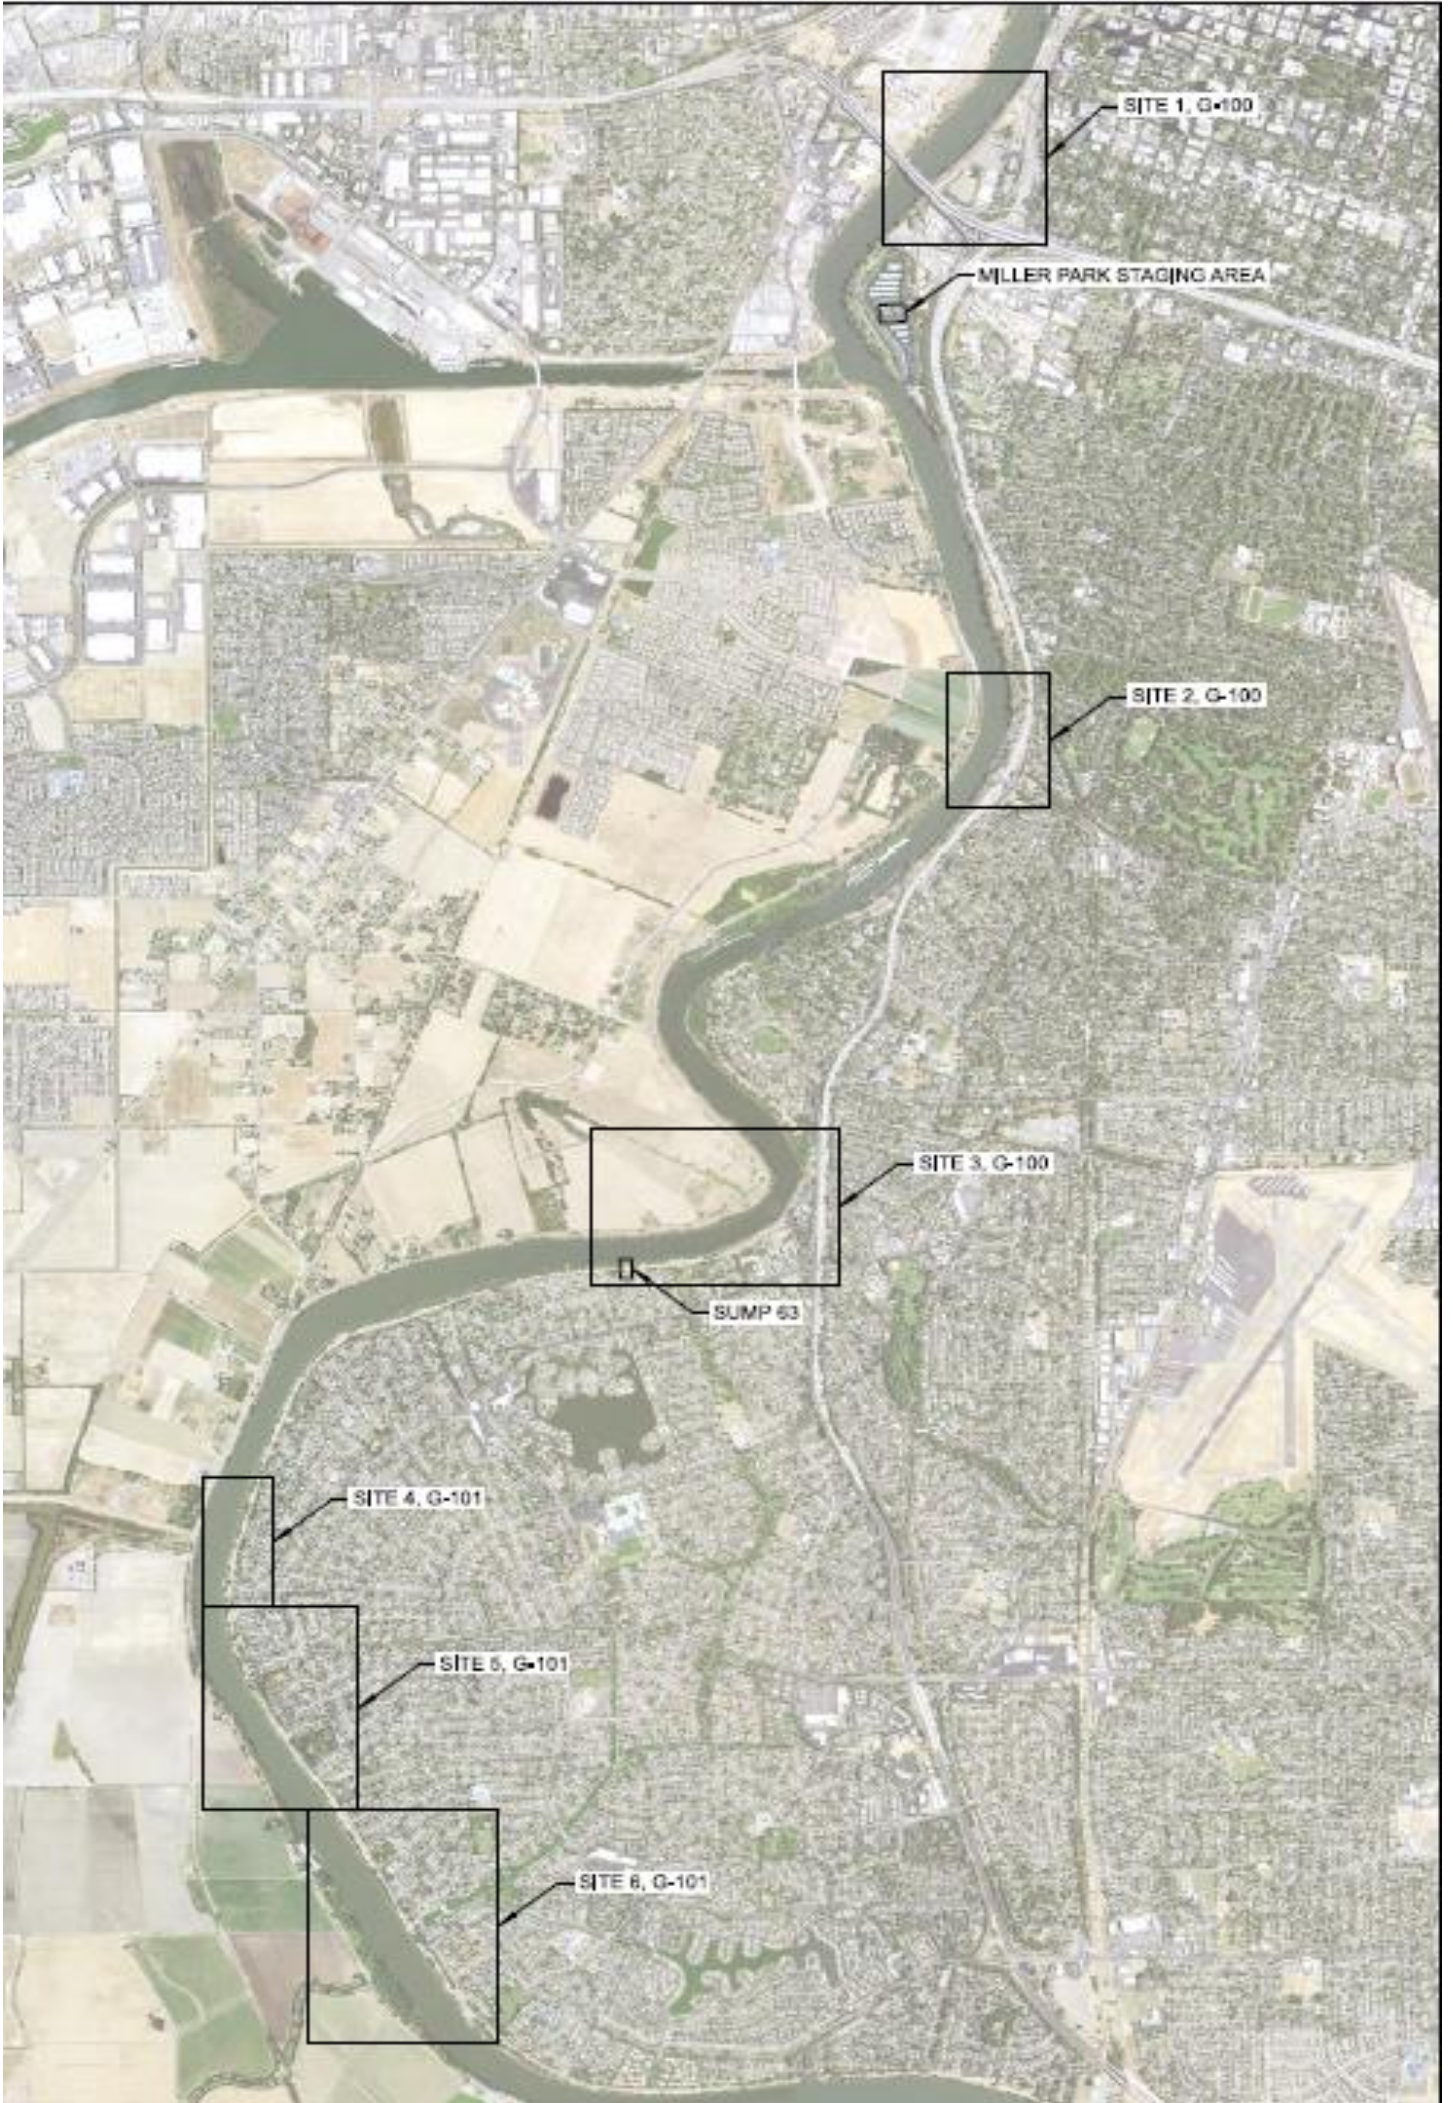

# Erosion C4 Construction Map

