

American River Common Features Natomas Basin

JULY 2023

Levee Improvement Project Monthly Update




US Army Corps
of Engineers®



U.S. ARMY

REACH	SCHEDULE
Reach A Gateway Oaks Dr to Farm Rd	<ul style="list-style-type: none"> FY23 Construction season underway along Garden HWY starting at Farm Rd. and extending to I-80. Additional tree removal resuming Fall 2023. Overhead Utility relocations ongoing, estimated completion Spring 2024. Improvements to Pumping Plant 1B, City Sump 160 and Pumping Plant 1A anticipated to begin in 2024. <p>Visit Reach A website for the latest project news: Click here</p>
Reach B San Juan Rd to Elverta Rd	<ul style="list-style-type: none"> Levee construction began July 2020; Adjacent Levee Construction is complete. Final completion, including seepage berm, is expected in the Fall 2023. Irrigation canal improvements are complete. Lift station is operational and new ARVs are installed. Additional programming and testing will be completed in Summer 2023. I-5 Window - Construction began Summer 2022 and was declared substantially complete in January 2023. Pumping Plants: <ul style="list-style-type: none"> Pumping Plant #3 – Construction completed, and plant is operational. Pumping Plant #5 - Construction expected to begin Summer 2024 Riverside Pumping Plant Replacement ongoing with discharge pipe relocation to begin 2024. Elkhorn Pumping Plant construction to begin 2024.
Reach C Elverta Rd to Sankey Rd	<ul style="list-style-type: none"> Levee construction was completed in 2008/2009 by Sacramento Area Flood Control Agency. Pritchard Lake Pumping Plant to begin construction in 2025.
Reach D Sankey Rd to Howsley Rd	<ul style="list-style-type: none"> Levee construction was completed in 2008/2009 by Sacramento Area Flood Control Agency. Highway 99 Window – Construction expected to begin Spring 2024. Pumping Plant #4 – Construction began August 2021; expected to be completed Fall 2023.
Reach E Howsley Rd to Sankey Rd	<ul style="list-style-type: none"> Construction activities began June 2023. Cutoff wall installation scheduled for Summer 2024. Natomas Levee Road is currently closed for construction activities from Sankey Road and extending north to Howsley Road.
Reach F&G Sankey Rd to Drainage Pumping Station	<ul style="list-style-type: none"> Levee construction and improvements to the levee slope and Pumping Plant #6 expected to begin Spring 2025.
Reach H Drainage Pumping Station to Northgate Blvd	<ul style="list-style-type: none"> Levee construction and improvements to Pumping Stations #8 and #102 began 2018; expected to be completed Spring 2023. Seepage berm construction to begin later Summer 2022; completion expected in the Spring 2023. Patrol Road & Fencing construction is underway.
Reach I Northgate Blvd to Gateway Oaks	<ul style="list-style-type: none"> Contract 1: Levee construction and improvements to Pump Station #58 completed Fall 2022. Contract 2: Landside levee improvements and installation of maintenance road expected to begin Summer 2024. <ul style="list-style-type: none"> Tree Removal efforts ongoing. Utility Relocations expected to begin in Summer 2023.

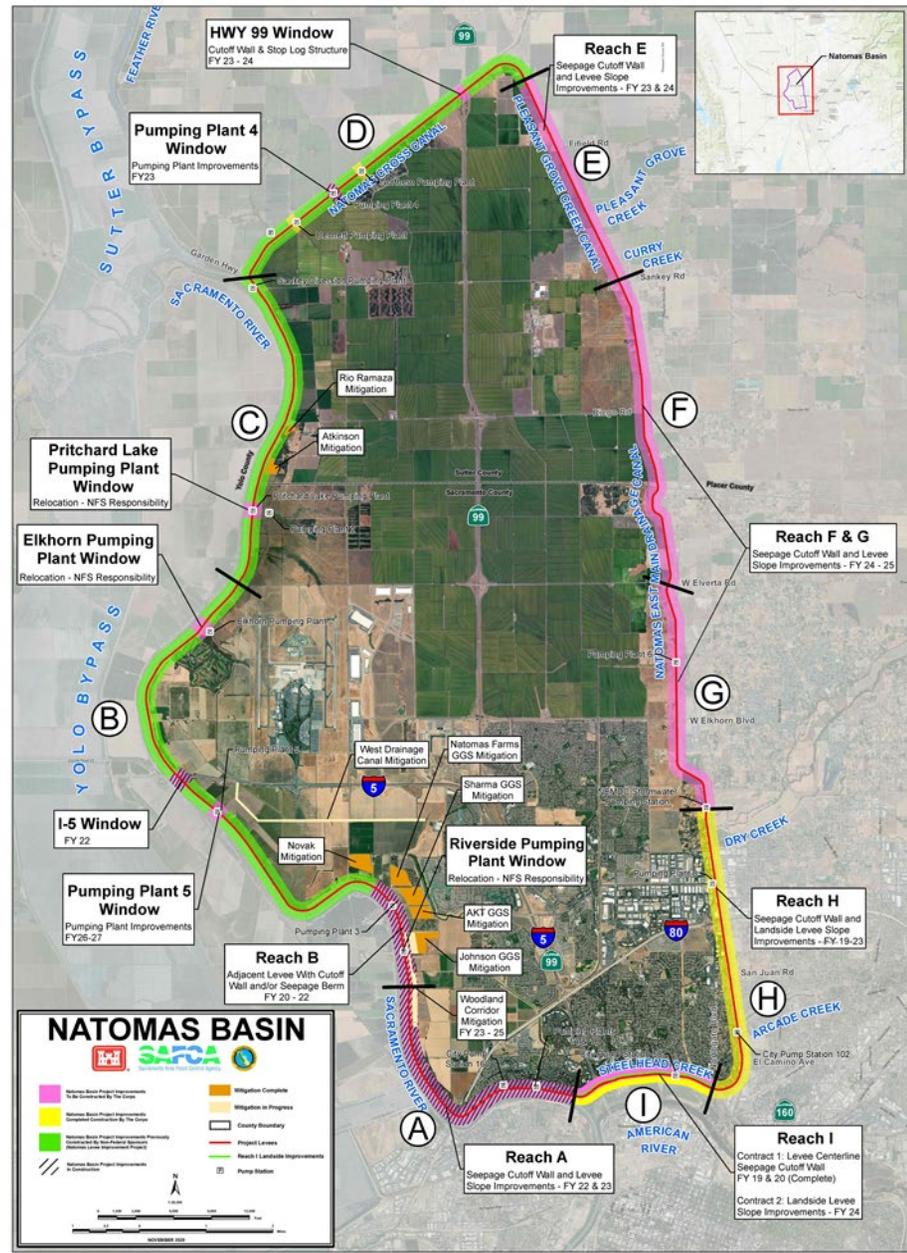

Get the Latest Natomas Updates Here



Project Website

www.natomaslevees.com

CONTACT INFORMATION

For questions or concerns, please contact USACE Public Affairs

916.557.5100 / spk-pao@usace.army.mil



US Army Corps
of Engineers®



American River Common Features Natomas Basin

Levee Improvement Project Monthly Update

APRIL 2023



US Army Corps
of Engineers®




U.S. ARMY



Reach B:

Pumping Plant No. 3 Relief Well Controlled Low Strength Material
backfill

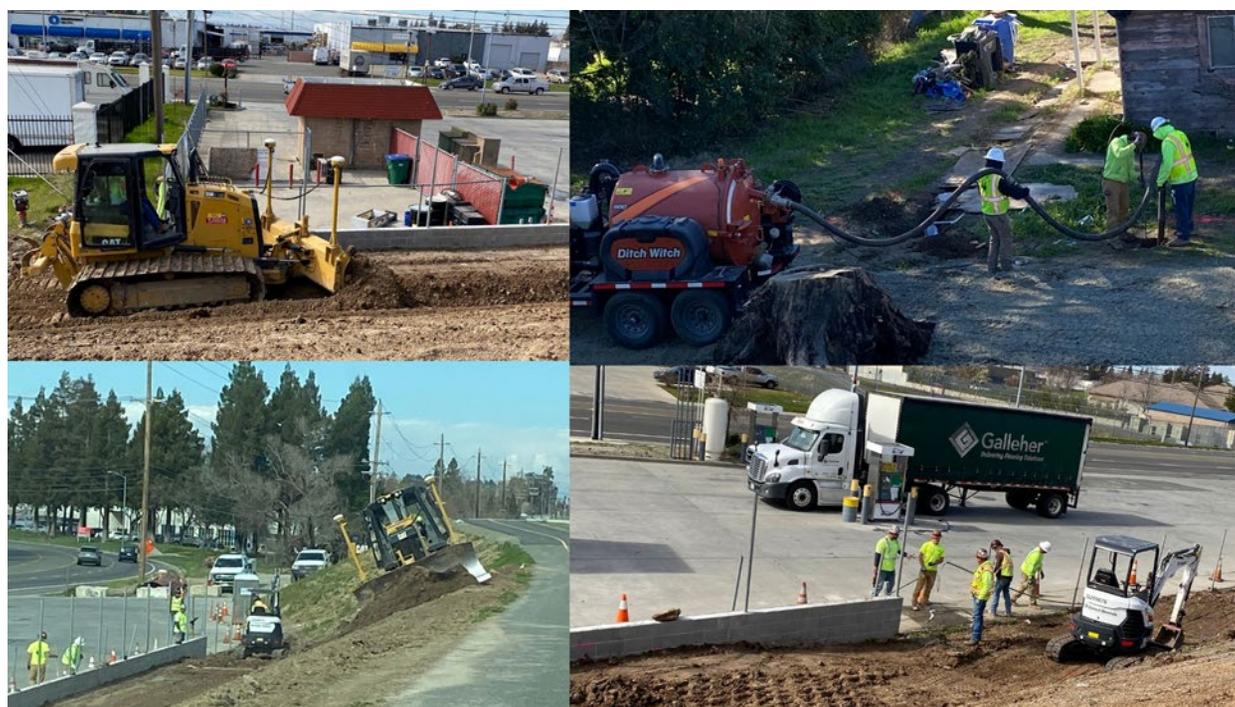

Reach H:

Levee improvements and Seepage Berm construction



US Army Corps
of Engineers®

