



American River Common Features 2016 American River Erosion Monthly Update August 2024

Highlights (last 30+ days)

Our Contract 3A (C3A) work is gearing up to get started soon. The 1986 high flow event (134k cfs) brought significant damage to the flood control system on the American river. This year we will address one of those areas which, although previously repaired, requires additional treatment to bring the site up to meet requirements for increased releases from Folsom dam.

Contract 3A (Site 1-1)

This contract will provide erosion protection at Site 1-1, which is on the left bank (South side) of the American River beneath and adjacent to the I-80 bridge.

During July and early August the contractor has been planning and getting approvals to begin work.

Other Prior Work

- Sites 2-1 and 2-3 Season 1 plus Mitigation sites at Paradise Bend, Rio Americano and Rossmoor West are being irrigated, maintained and monitored for performance as vegetation establishment continues.
- Site 2-3 season 2 and site 2-2 will have vegetation installed this summer.


Looking Ahead (next 30+ days)

Current Activity - What can I expect?

Work hours: Monday-Saturday from 7 a.m. to 6 p.m. and Sunday 9 a.m. to 6 p.m.

Contract 3A (Site 1-1)

Preparation to begin work at Site 1-1 has proven challenging but we should start work by the end of August. Mobilization will include setting up construction trailers, establishing staging areas and installing safety fencing. When haul does begin, loaded construction haul vehicles will enter the erosion work site from Sutter's Landing and will egress empty via Glenn Hall Park. The temporary access driveway established in 2022 at Glenn Hall Park will remain in place through 2024 for completion of the Site 1-1 erosion protection work. Access to Paradise Beach will be maintained as it has in the past. The levee crown between Sutter's Landing and Glenn Hall Park will be closed to pedestrian traffic during the construction period. Dust control and speed limits will be in effect.

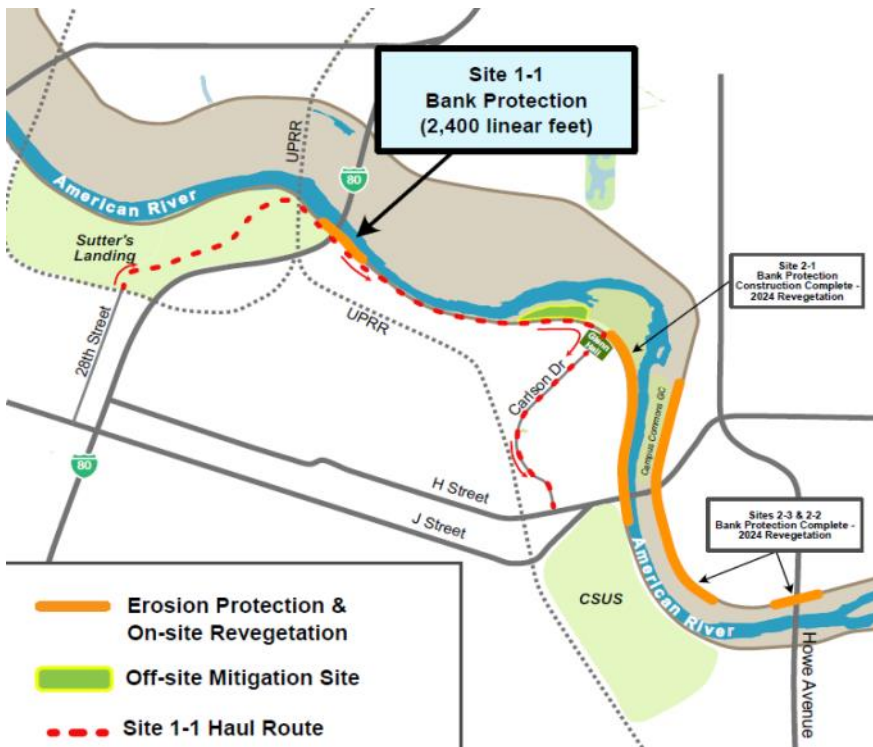

Information Resources:

Project Webpage:

www.sacleveeupgrades.com



Contact Information:

For questions or concerns, contact
Public Affairs: [916-557-5100](tel:916-557-5100)
spk-pao@usace.army.mil

Upcoming Milestones

LAR Contract C3A

Construction
August - November 2024

LAR Contract 2

Site 2-3 Season 2, Site 2-2
Revegetation
Summer 2024

LAR Contract C3A

Revegetation
Spring-Summer 2025

Additional information regarding this project can be found at
www.sacleveeupgrades.com

**All Dates Subject to Change*
