



American River Common Features 2016 Sacramento River Levees Monthly Update

DEC 2023

Highlights (last 30 days)

Sacramento River Erosion (SRE): Contract 2 Season 1 is complete. Contract 4 bids were received. Contract 2 Season 2 and Contract 4 are on track for 2024 construction!

Sacramento River East Levee (SREL): Contract 3 is complete. Contract 4 is over 85% complete and will continue into 2024 due to project delays near the Westin Hotel.

Looking Ahead (next 30+ days)

What can I expect?

SRE
Tree cutting through February 15, 2024, in preparation for Contract 2 Season 2. Note: There is no need to cut trees in preparation for Contract 4.

SREL
Production Jet Grout drilling will continue at Garcia Bend Park and Sump 132 and complete by mid-January 2024. Jet Grouting at Westin Hotel will resume and continue into 2024.

Hours of Operation: Mon – Sat from 7 a.m. - 7 p.m.

Garcia Bend Park Staging
◆ Boat ramp closed during construction at the City’s request with intermittent vehicle traffic during construction.
◆ Garcia Bend Park will have light traffic in and out until the end of the year.
◆ Jet Grout cutoff wall work has resumed and will be ongoing until end of December. Anticipate 20-30 truckloads of spoils off-hauled out of Garcia Bend Park throughout construction.

Sump 132
◆ Work anticipated to continue through December.
◆ Drilling at Sump 132 and spoils management at Garcia Bend Park will be occurring during this time.

Cliff’s Marina
◆ All work from Cliff’s Marina to Freeport Bridge is complete.

Westin
◆ Levee cutoff wall work will continue through May 2024 due to delays in construction.
◆ Sump 41 pump station construction is complete.

Question of the Month

In preparation for the coming construction season, tree clearing is completed from November 1—February 15. What drives this date range?

Birds like the hawk, magpie, and osprey tend to nest during the same period (late February through October). The Migratory Bird Treaty Act of 1918 prohibits killing, capturing, or handling protected bird species, including their nests and eggs.

While we can technically survey for birds and remove trees at anytime during the year, removing trees from November 1—February 15 is a best practice. If we discover a tree requiring removal during the avoidance period (late February through October), it cannot contain an active nest and a bird monitor is required to be onsite during removal activities.

Information Resources:

Project Webpage:
www.sacleveeupgrades.com



Sacramento District Homepage:
www.spk.usace.army.mil

Contact Information:
For questions or concerns, please contact our Public Affairs Office at
916-557-5100
spk-pao@usace.army.mil

Upcoming Milestones

Seepage/Stability/ Overtopping

SREL Contract 3
Construction
March 2022 - October 2023

SREL Contract 4
Construction
April 2023 - May 2024

Erosion

Contract 2
Season 2 Tree Trimming
February 2024

Construction
July 2023 - October 2024


Contract 3
Construction Contract Award
Anticipated January/February
2025

Contract 4
Construction Contract Award
Anticipated January/February
2024

Additional information can be found on our project web page at www.sacleveeupgrades.com

*All Dates Subject to Change

SREL Contract 4 Construction Map

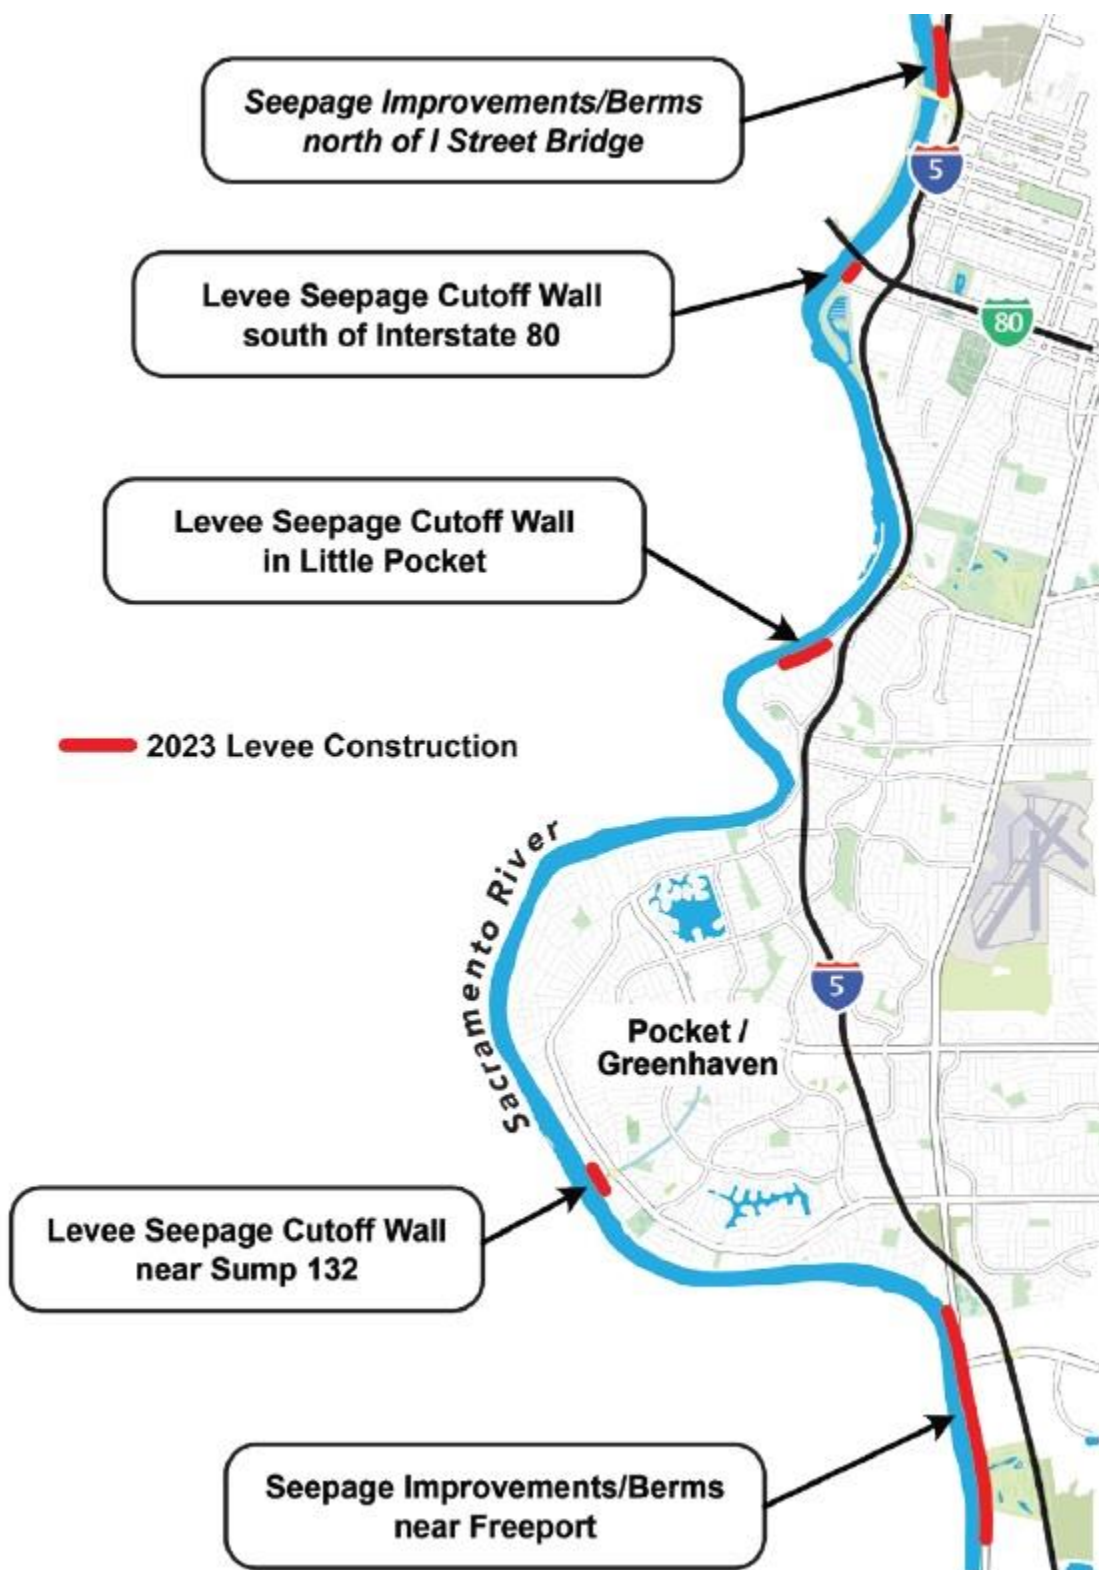

Erosion C2 Construction Map

