



American River Common Features 2016 American River Erosion Monthly Update

December 2022

Highlights (last 30+ days)

Contract 1 (Site 2-1)

Rock Slope protection (on the bank and levee) and installation of in stream wood material on erosion control fabric completed in November. This brings to an end, major haul traffic so the electronic signage on Carlson was removed.

Contract 2 (Site 2-3, Season 1)

The site, including campus commons golf course and parking lot, has been secured for the winter. The bike detour will remain in place to accommodate later contracts this fall and next spring (2023).

Looking Ahead (next 30+ days)

Current Activity - What can I expect?

Work hours: Monday-Saturday from 7 a.m. to 6 p.m. and Sunday 9 a.m. to 6 p.m.

Contract 1 (Site 2-1)

The Operations and Maintenance (O&M) road will be completed followed by final placement of rock and aggregate base. Soil fill and topsoil placement will be completed on Rock slope protection followed by erosion control fabric, and hydroseeding. Minor hauling of remaining topsoil and aggregate base will be required. January will see site final seeding, clean up, demobilization and removal of fencing.

Contract 2 (Site 2-3, Season 1)

Site 2-3 S1 will remain dormant while preparations for Season 2 (Site 2-2,2-3) will begin with elderberry transplanting and vegetation clearing within the project footprint. This will affect sites from H Street bridge to the Howe Avenue bridge (see map).

Mitigation E1A (Paradise Bend)

Clearing of invasive vegetation will begin at the Paradise Bend mitigation site to prepare the site to receive Elderberry transplants from the future Contract 3A bank protection site at the I-80 bridge. Pedestrian activity will only be restricted in active work areas.

Question of the Month

What can we expect for next year? Why is the access point remaining at Glenn Hall Park?

Another erosion site, known as Contract C3A, will be constructed in 2023 at the west end of the River Park Neighborhood near the I-80 bridge. The site is about half the size of C1 and includes a similar design. Egress will be through Glenn Hall Park so the same access point is being retained. Public access to all facilities including Paradise Beach will be maintained.

Information Resources:

Project Webpage:

www.sacleveeupgrades.com




Contact Information:

For questions or concerns, contact

Public Affairs: 916-557-5100

spk-pao@usace.army.mil

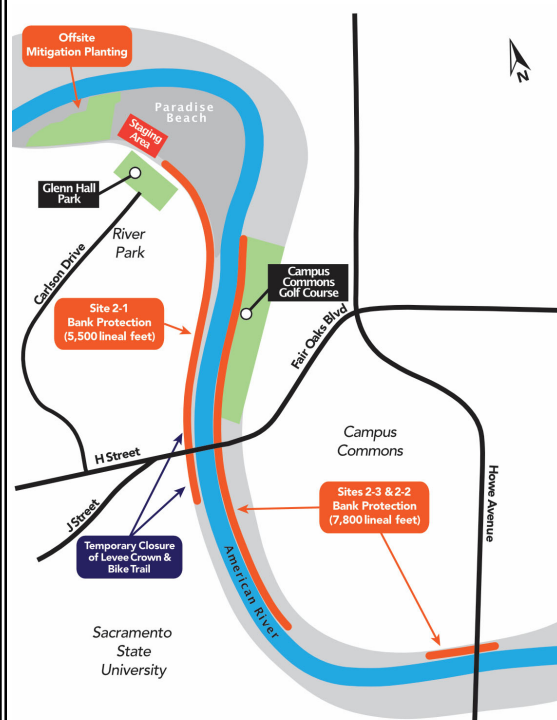

Upcoming Milestones

LAR Contract 1

Construction

May - January 2022

LAR Contract 2

Construction (Season 2)

April - October 2023

Mitigation E1A

Vegetation Clearing

November - February 2023

Additional information regarding our ongoing project can be found on our project web page at

www.sacleveeupgrades.com

**All Dates Subject to Change*
